# 5991-08-11 DOT Onalaska CTH OT
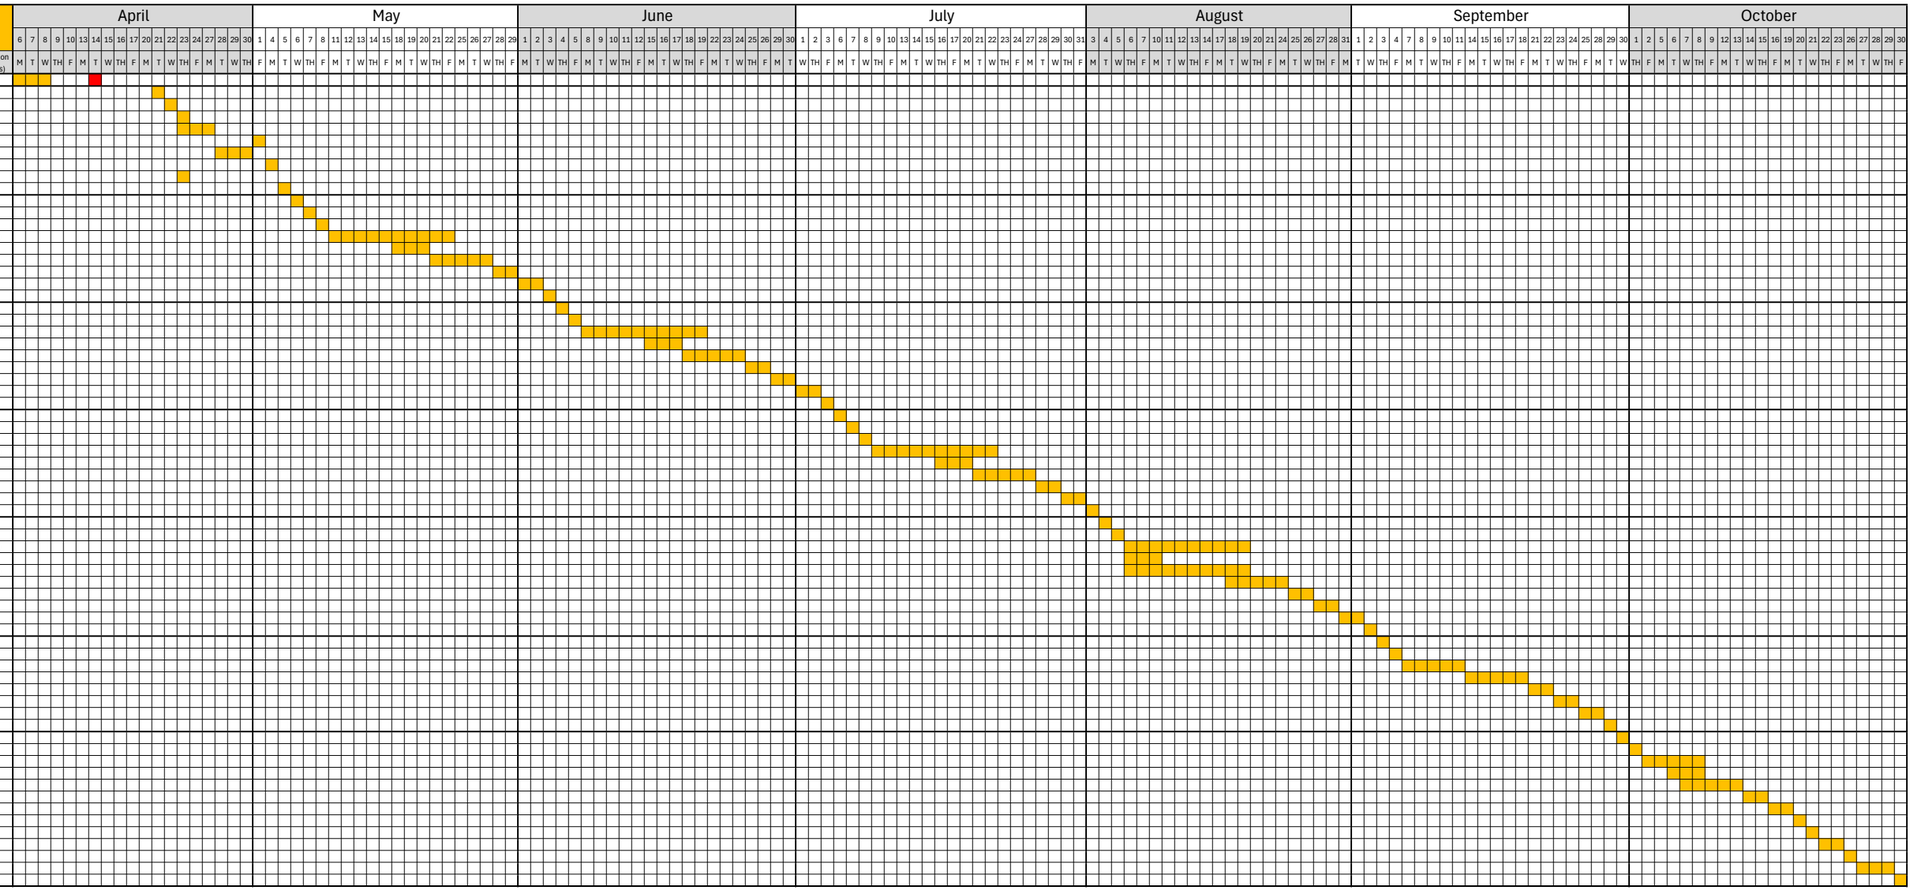
| Stage | Task | Contractor | Duration (Days) |
|---|---|---|---|
| **Project** | Clearing and Grubbing | Gerke | 3 |
| 1 | Traffic Control Set up | Forward | 1 |
| | Erosion Control Install | Smith | 1 |
| | Sawcutting | Con Cor | 1 |
| | Corporate Drive Grading | Gerke | 3 |
| | Corporate Drive Paving | Mathy | 1 |
| | Island Removals and Grading | Gerke | 3 |
| | Island Temp Paving | Mathy | 1 |
| | Guardrail work at overpass eastbound | Smith | 1 |
| | Restoration | Smith | 1 |
| 2a | Traffic Control & Temp Pavement Marking Set up | Forward | 1 |
| | Erosion Control Install | Smith | 1 |
| | Sawcutting | Con Cor | 1 |
| | Grading and Storm Sewer | Gerke | 10 |
| | Electrical | Poellinger | 3 |
| | Curb and Flatwork install | Chippewa | 5 |
| | Topsoil | Gerke | 2 |
| | Restoration | Smith | 2 |
| | Temp Paving | Mathy | 1 |
| 2b | Traffic Control & Temp Pavement Marking Set up | Forward | 1 |
| | Sawcutting | Con Cor | 1 |
| | Grading and Storm Sewer | Gerke | 10 |
| | Electrical | Poellinger | 3 |
| | Curb and Flatwork install | Chippewa | 5 |
| | Topsoil | Gerke | 2 |
| | Restoration | Smith | 2 |
| | Guardrail work | Smith | 2 |
| | Paving Binder | Mathy | 1 |
| 3a | Traffic Control & Temp Pavement Marking Set up | Forward | 1 |
| | Erosion Control Install | Smith | 1 |
| | Sawcutting | Con Cor | 1 |
| | Grading and Storm Sewer | Gerke | 10 |
| | Electrical | Poellinger | 3 |
| | Curb and Flatwork install | Chippewa | 5 |
| | Topsoil | Gerke | 2 |
| | Restoration | Smith | 2 |
| | Temp Paving | Mathy | 1 |
| 3b | Traffic Control & Temp Pavement Marking Set up | Forward | 1 |
| | Sawcutting | Con Cor | 1 |
| | Grading and Storm Sewer | Gerke | 10 |
| | Electrical | Poellinger | 3 |
| | Retaining Wall Build | Smith | 10 |
| | Curb and Flatwork install | Chippewa | 5 |
| | Topsoil | Gerke | 2 |
| | Restoration | Smith | 2 |
| | Guardrail work | Smith | 2 |
| | Paving Binder | Mathy | 1 |
| 3c | Traffic Control & Temp Pavement Marking Set up | Forward | 1 |
| | Sawcutting | Con Cor | 1 |
| | Grading | Gerke | 5 |
| | Curb and Flatwork install | Chippewa | 5 |
| | Topsoil | Gerke | 2 |
| | Restoration | Smith | 2 |
| | Guardrail work | Smith | 2 |
| | Paving Binder | Mathy | 1 |
| 4 | Traffic Control & Temp Pavement Marking Set up | Forward | 1 |
| | Sawcutting | Con Cor | 1 |
| | Removals and Grading for Islands and Center Circle | Gerke | 5 |
| | Electrical | Poellinger | 3 |
| | Curb and Flatwork install | Chippewa | 5 |
| | Topsoil | Gerke | 2 |
| | Restoration | Smith | 2 |
| | Signs | Smith | 1 |
| | Milling | All States | 1 |
| | Paving Surface | Mathy | 2 |
| | Pavement Markings | Forward | 1 |
| | Misc Punchlist | All | 3 |
| | Remove Traffic Control | Forward | 1 |
